K-1070-F

ND:00005

Waste Disposal In Contractor's Burial Grounds
(Includes Special Waste and Tentatively Planned Disposal Waste)

operation 5 years

ITEM	VOLUME
Building and Construction Debris	60,000 cubic ft/yr or 240 cubic ft/day
TSCA Incinerator Site Work Debris	540,000 cubic ft (work completed 3-1-85)
Wet Concrete	1,620 cubic ft/yr or 6.5 cubic ft/day
Asbestos (tentatively planned for disposal)	4,000 square ft/yr or 16 square ft/day
Glass and Plastic (tentatively planned for disposal)	2,400 lbs/yr or 9.6 lbs/day
Paint Cans	2,400 lbs/yr or 9.6 lbs/day
Empty Cans (aerosol)	400 lbs/yr or 1.6 lbs/day
Coal Pile Runoff, Neutralized (tentatively planned for disposal)	200,000 gallons/yr or 803 gallons/day
Fly Ash	26,500,000 lbs/yr or 106,425 lbs/day
Lime Sludge (tentatively planned for disposal)	2,100 lbs/yr or 8.4 lbs/day
Process Cooling Water, Centrifuge Program	6,000 gallons/yr or 24 gallons/day
RCW Clarifier Blowdown Sludge (tentatively planned for disposal)	3,735,000 lbs/yr or 15,000 lbs/day
Waste Oil (dust control)	24,000 gallons/as available

*Calculations based on 249 working days per year per J. K. Bailey request.

APPROVAL FOR RELEASE

Document: # Unnumbered; Date ND;

Title/Subject Waste Disposal in Contractor's Burial Grounds (Includes Special Waste ...), 1 page and Drawing # ES-22813AF/R0.

Approval for unrestricted release of this document is authorized by the Oak Ridge K-25 Site Classification and Information Control Office, Martin Marietta Energy Systems, Inc., PO Box 2003, Oak Ridge, TN 37831-7307.

K-25 Classification & Information Control Officer — Date 1/26/95

#762

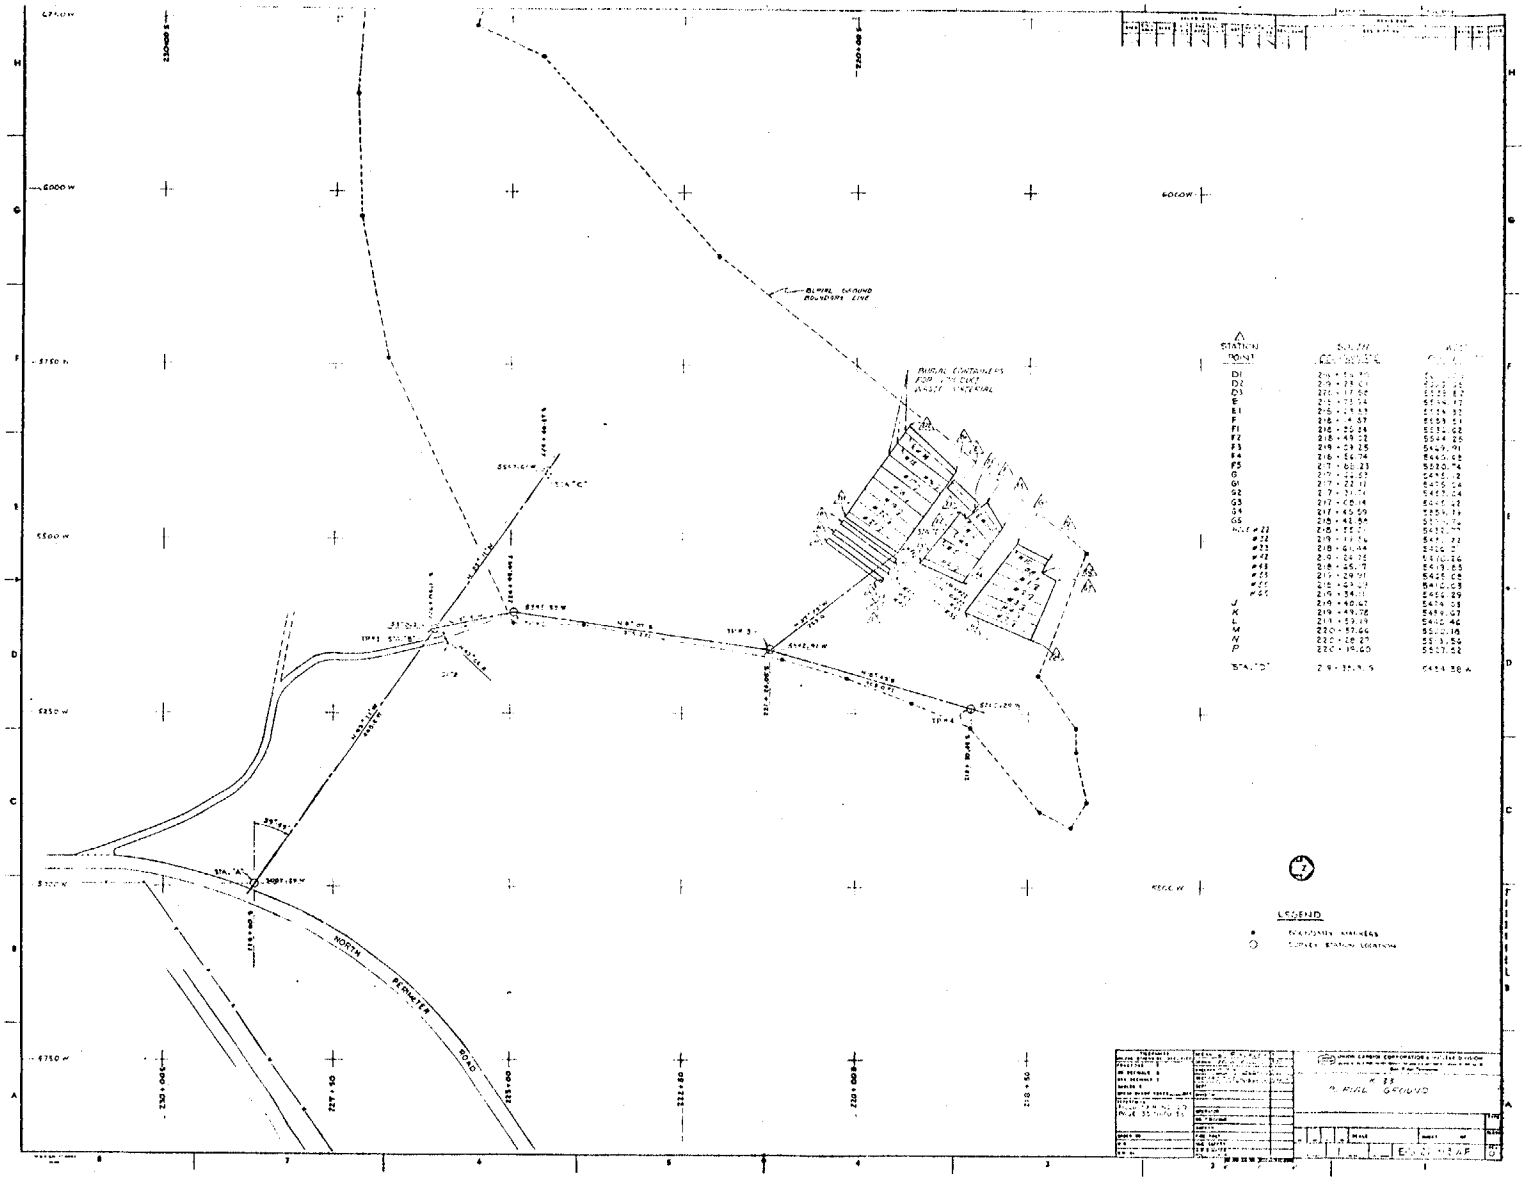
NORTH PERIMETER ROAD
LEGEND
